

ESPAÑA

AIP-ESPAÑA

AIS-ESPAÑA

Dirección AFTN: LEANZXTA

Teléfono: +34 913 213 363

E-mail: ais@enaire.es

Web: www.enaire.es

ENAIRE

DIVISIÓN DE INFORMACIÓN AERONÁUTICA

c/ Campezo, 1. EDIFICIO 2

Kudos Innovation Campus Las Mercedes

28022 Madrid (ESPAÑA)

SUP 134/26

AIRAC 23-JUL-26

EFFECTIVE DATE WEF 03-SEP-26

AD

SUP 134/26

03SEP26/03SEP27EST

NOTE: EST SUP will only be cancelled by NOTAM, SUP or AIP amendment.

ZARAGOZA AD (LEZG).- New markings on aprons.

1. INTRODUCTION

Until 03 September2027 (estimated), works to paint new horizontal markings on the apron and repaint existing markings will be underway.


The works will be carried out by areas which will correspond to the different phases and sub-phases to minimise/eliminate operational impact. The start, end and activation dates of the different phases/sub-phases of these works, as well as any operational incidents that may arise, will be announced via NOTAM.

All work areas shall be duly marked and lit. Caution is recommended due to the presence of workers and machinery and earthworks.

Scope of the works:

- Painting new horizontal markings on the apron and repainting existing markings.

The works will be performed in the areas highlighted in the map:

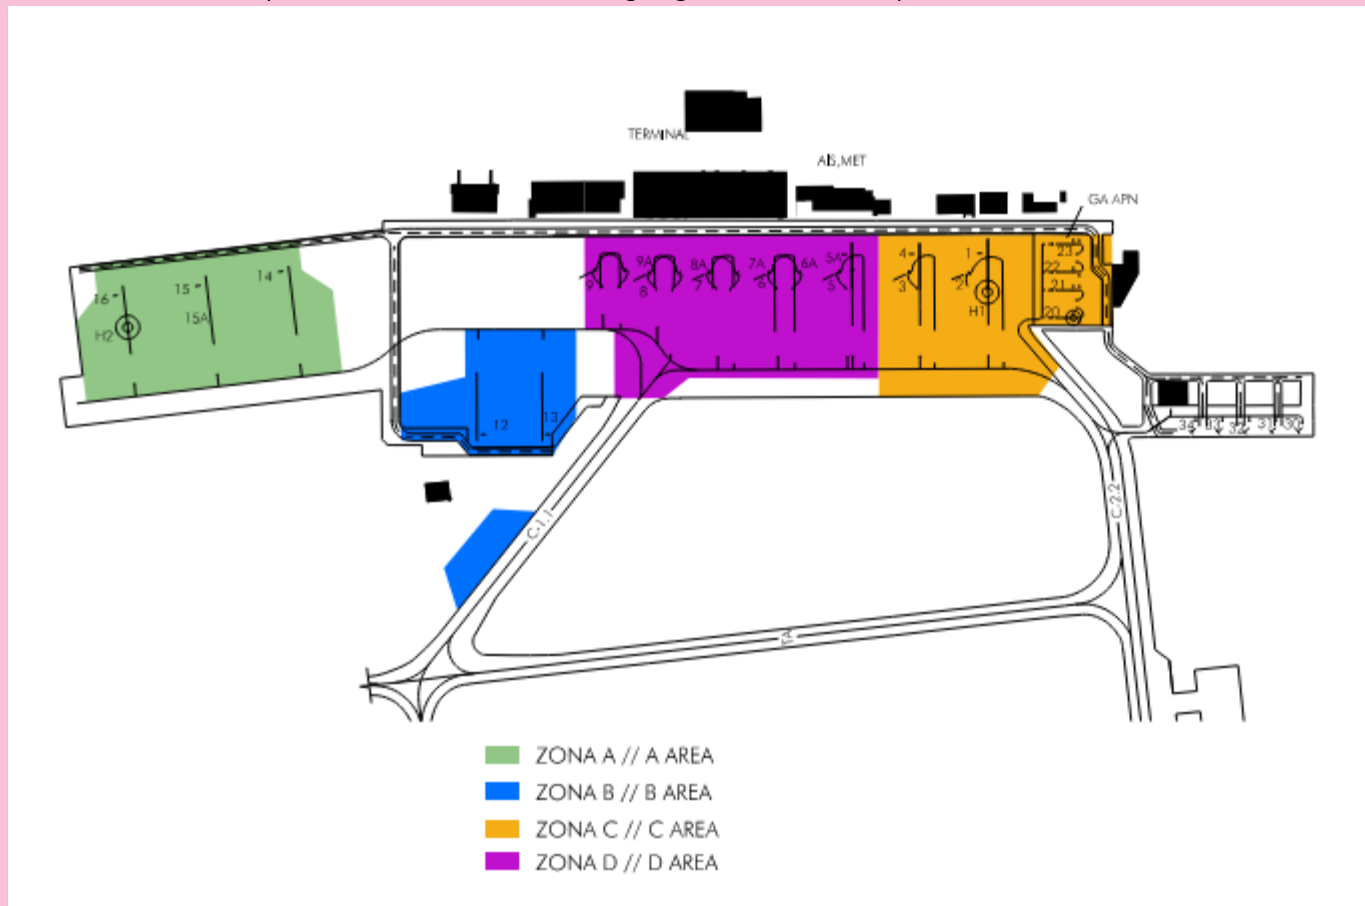

2. PHASES

PHASE 1. PRIOR ACTIONS, STAKEOUT AND WORK SITE ASSEMBLY

Works to assemble the work site.


Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- No operational impact.

PHASE 2. AREA A (PRKG 14, 15 and 16)

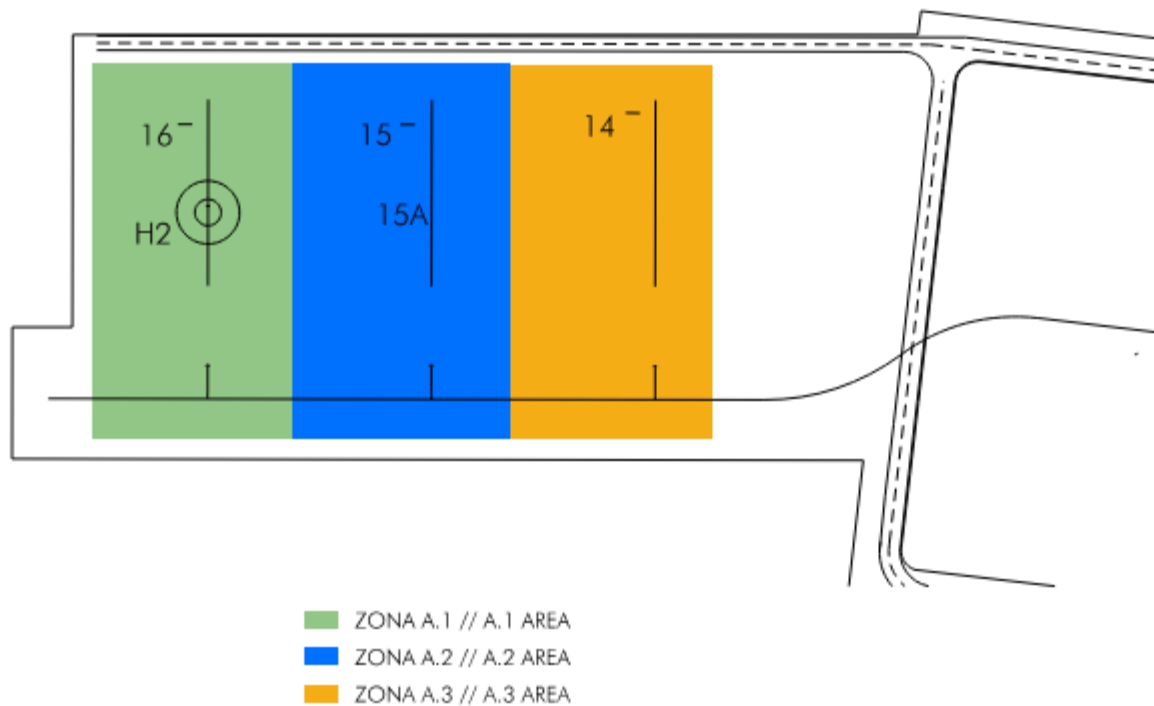

SUB-PHASE 2.1 AREA A.1

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 16 and H2 due to the works.

SUB-PHASE 2.2 AREA A.2

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 15 due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 15, 16 and H2.

SUB-PHASE 2.3 AREA A.3


Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 14 due to the works
- Closure of the inner taxiway section leading to/out of PRKG 14, 15, 16 and H2.

PHASE 3. AREA B (PRKG 12, 13, service road and RFFS)

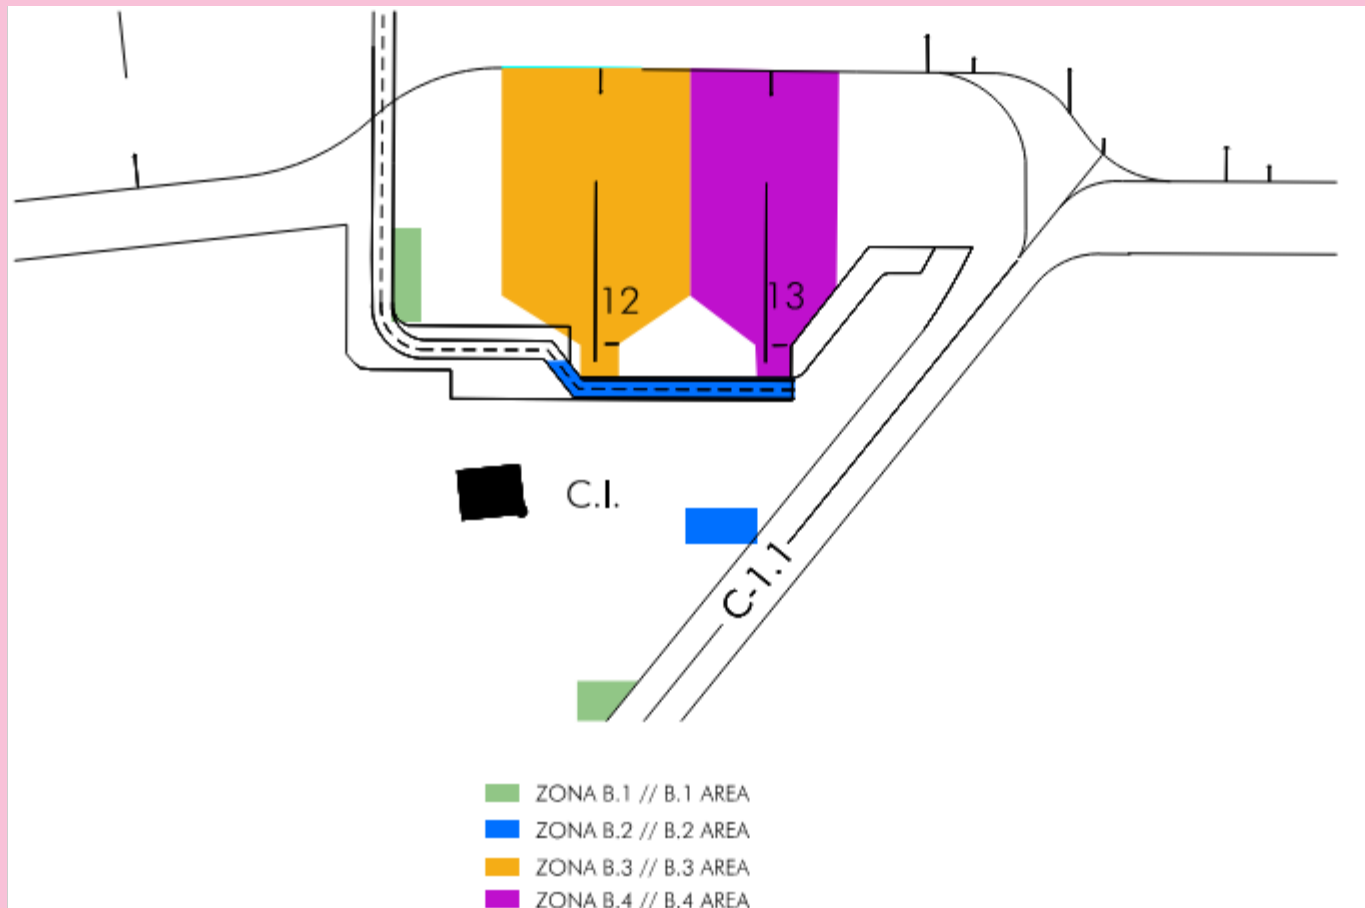

SUB-PHASE 3.1 AREA B.1

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- South access to TWY C11 from RFFS building unavailable.

SUB-PHASE 3.2 AREA B.2

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- East access to TWY C11 from RFFS building unavailable.

SUB-PHASE 3.3 AREA B.3

Schedule:

- This phase will be executed during the airport's operational hours.


Operational restrictions:

- Closure of PRKG 12 due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 12, 14, 15, 16 and H2.

SUB-PHASE 3.4 AREA B.4 Schedule:

- This phase will be executed during the airport's operational hours. Operational restrictions:
- Closure of PRKG 13 due to the works
- Closure of the inner taxiway section leading to/out of PRKG 12, 13, 14, 15, 16 and H2.

PHASE 4. AREA C (ROADWAY AREA FUEL LOADING FACILITY, PRKG 20-23, AND 1-4)

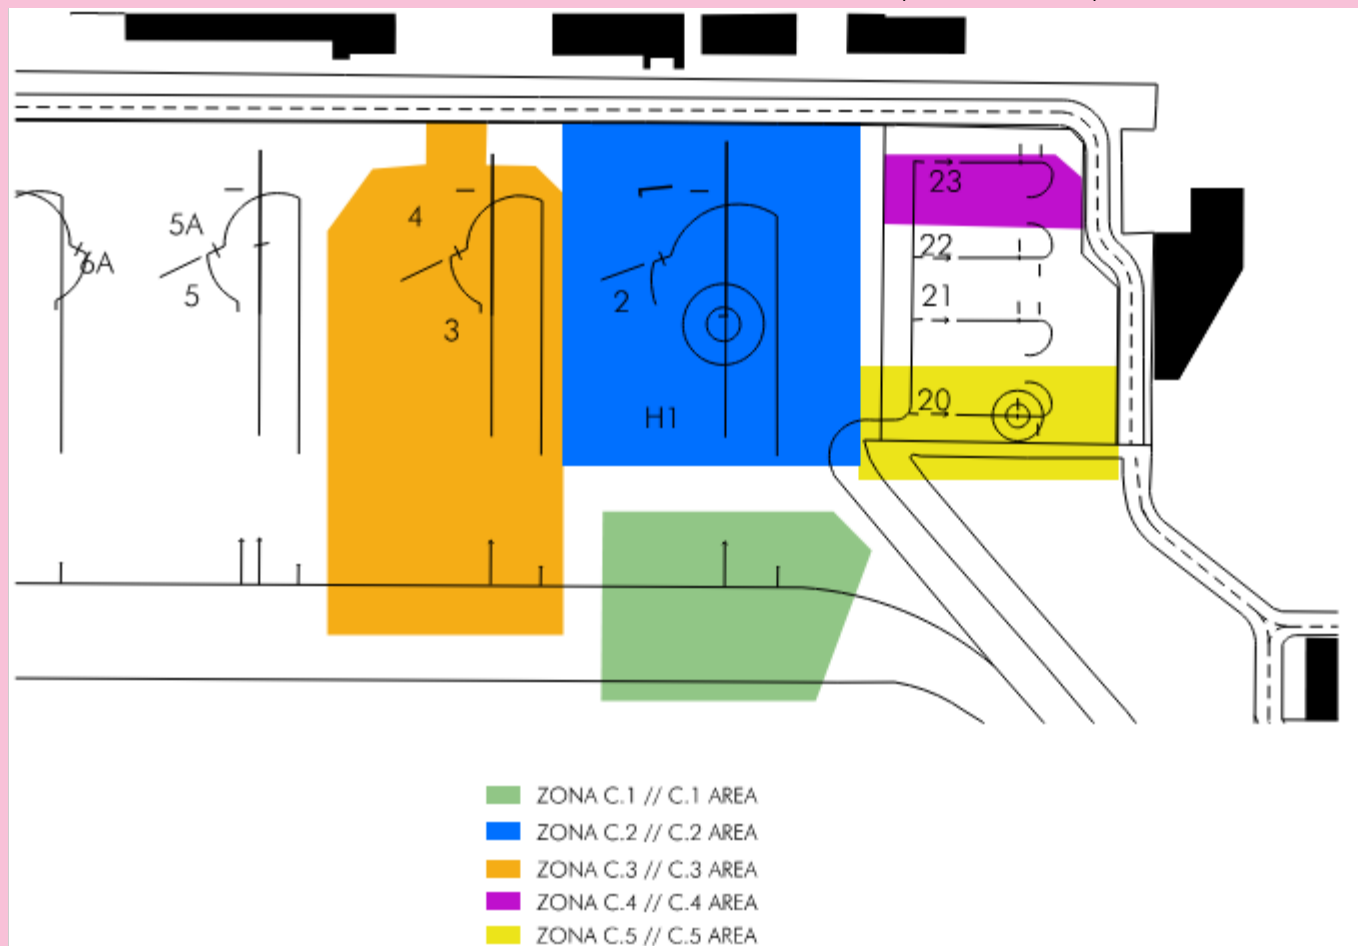

SUB-PHASE 4.1 AREA C.1

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of the inner taxiway section leading to/out of PRKG 1, 2, H1, 20-23 and H3
- Closure of TWY C22.
- Entry to/exit from rest of the PRKG via TWY C11.

SUB-PHASE 4.2 AREA C.2

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 1, 2 and H1 due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 20, 21, 22, 23 and H3.

SUB-PHASE 4.3 AREA C.3

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 3 and 4 due to the works.
- Entry to/exit from PRKG 5, 5A, 6, 6A, 7, 7A, 8, 8A, 9, 9A, 11, 12, 13, 14, 15, 16 and H2 via TWY C11.
- Entry to/exit from PRKG 1, 2, H1, 20, 21, 22, 23 and H3 via TWY C22.

SUB-PHASE 4.4 AREA C.4

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 22 and 23 due to the works.

SUB-PHASE 4.5 AREA C.5


Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 20 and H3 due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 20-23 and H3.

PHASE 5. AREA D (PRKG 5-9A, SERVICE ROAD AND PEDESTRIAN ROAD)

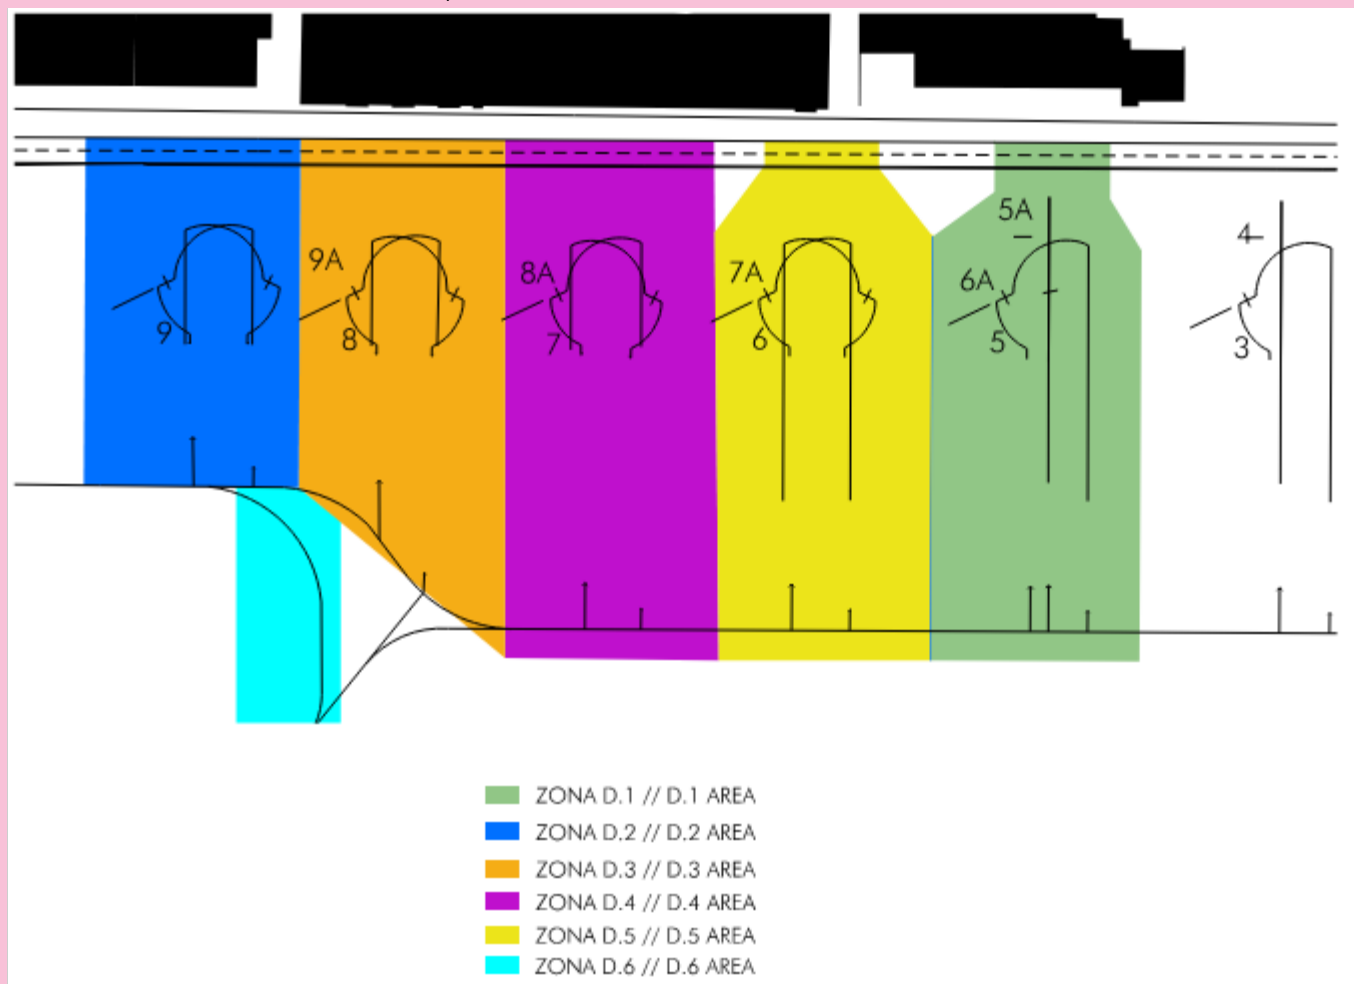

SUB-PHASE 5.1 AREA D.1

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 5 and 5A due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 5 and 5A.
- Entry to/exit from PRKG 6, 6A, 7, 7A, 8, 8A, 9, 9A, 11, 12, 13, 14, 15, 16 and H2 via TWY C11.
- Entry to/exit from PRKG 1, H1, 2, 3, 4, 20, 21, 22, 23 and H3 via TWY C22.

SUB-PHASE 5.2 AREA D.2

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 9, 9A due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 9, 9A, 12, 13, 14, 15, 16 and H2.

SUB-PHASE 5.3 AREA D.3

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 8, 8A due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 8 and 8A.
- Entry to/exit from PRKG 1, 1A, 1B, 1C, H1, 2, 3, 4, 5, 5A, 6, 6A, 7, 7A, 20, 21, 22, 23 and H3 via TWY C22.
- C11 closed for the duration of works on the inner taxiway.

SUB-PHASE 5.4 AREA D.4

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 7, 7A due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 7 and 7A.
- Entry to/exit from PRKG 1, H1, 2, 3, 4, 5, 5A, 6, 6A, 20, 21, 22, 23 and H3 via TWY C22.
- Entry to/exit from PRKG 8, 8A, 9, 9A, 12, 13, 14, 15, 16 and H2 via TWY C11.

SUB-PHASE 5.5 AREA D.5

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of PRKG 6, 6A due to the works.
- Closure of the inner taxiway section leading to/out of PRKG 6 and 6A.
- Entry to/exit from PRKG 1, H1, 2, 3, 4, 5, 5A, 20, 21, 22, 23 and H3 via TWY C22.
- Entry to/exit from PRKG 7, 7A, 8, 8A, 9, 9A, 12, 13, 14, 15, 16 and H2 via TWY C11.

SUB-PHASE 5.6 AREA D6

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- Closure of TWY C11.
- Closure of the inner taxiway section leading to/out of PRKG 9, 9A, 12, 13, 14, 15, 16 and H2.
- Entry to/exit from PRKG 1, H1, 2, 3, 4, 5, 5A, 6, 6A, 7, 7A, 8, 8A, 20, 21, 22, 23 and H3 via TWY C22.

PHASE 6 FINAL CLEANING AND CLEARING OF AREA

Works to remove the construction site, compliance and clearing of the area.

Schedule:

- This phase will be executed during the airport's operational hours.

Operational restrictions:

- No operational impact
